

Community Restroom Project

Schematic Design, Budget and Schedule

June 17, 2021



Scope of Work

Scope of Work

- Installation of one (1) prefabricated community restroom building and associated sitework at the following locations:
 - Castro/Mistral Elementary School
 - Huff Elementary School
 - Landels Elementary School
- Each Restroom building will have two (2) single occupancy restrooms with standard finishes.



Proposed Plans

Proposed Building



Castro/Mistral Elementary School Location













Huff Elementary School Location

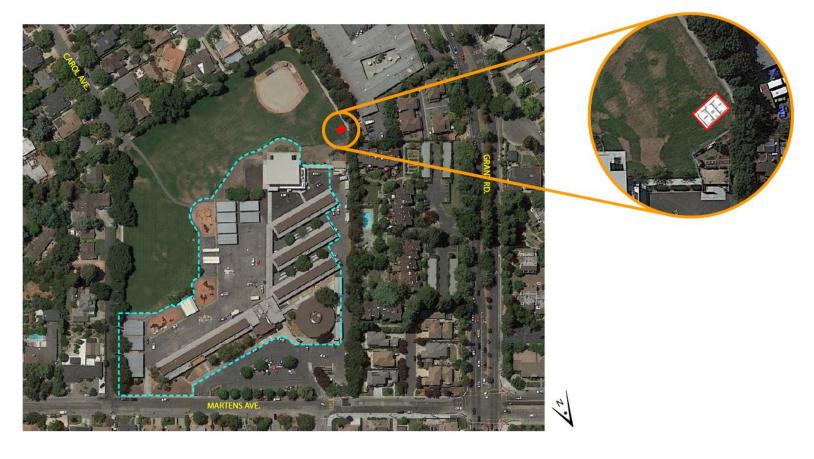



Landels Elementary School Location





LANDELS ELEMENTARY

MOUNTAIN VIEW WHISMAN SCHOOL DISTRICT

NEW PARK RESTROOM MODULAR BUILDING
NTS





Proposed Budget

Schematic Design Budget

#	Description	Quantity Unit	Unit \$	Total	
	1 Huff Site Development	1 ls	\$ 85,000	\$	85,000
	2 Landels Site Devlopment	1 s	\$ 75,000	\$	75,000
	3 Mistral Site Development	1 ls	\$ 105,000	\$	105,000
	4 Modular Toilet Rooms	3 ea	\$ 192,000	\$	576,000
	5 Anticipated bid amount	1 ls		\$	841,000

Project Cost

Description	Quantity		U	nit Cost	Subtotal
Construction Budget	1	ls			\$ 841,000
Design Contingency	10	%			\$ 84,100
Construction Contingency	10	%			\$ 84,100
Architect Fees	1	ls			\$ 45,600
Architect Contingency	1	ls			\$ 12,615
Architect Reimbursable Expenses	1	ls			\$ 3,192
Blueprinting	1	ls			\$ 2,500
Topographic Survey	1	ls	\$	15,000	\$ 15,000
Soils Report & Testing	1	%			\$ 8,410
CM Fees	4.5	%			\$ 37,845
DSA Inspector	3	mos.	\$	15,000	\$ 45,000
Testing Laboratory	1	%			\$ 8,410
Bid Advertisements	1	ls			\$ 2,500
DSA Fees	1.2	%	\$	1,009,200	\$ 12,110
CGS Fees	3	ea	\$	3,600	\$ 10,800
CEQA	1	ls	\$	2,500	\$ 2,500
Legal	1	ls	\$	5,000	\$ 5,000
Misc. Expenses	1	ls	\$	5,000	\$ 5,000
Grand Total					\$ 1,225,682



Schedule

Schedule

Task Name	Duration	Start	Finish	
Community Restrooms at Castro/Mistral, Huff and Landels ES	314 days	Mon 11/16/20	Thu 1/27/22	
Schematic Design	75 days	Mon 11/16/20	Fri 2/26/21	
Review Process with District stakeholders and City	60 days	Mon 3/1/21	Fri 5/21/21	
BOT Info - SD Approval	1 day	Thu 6/3/21	Thu 6/3/21	
BOT Action SD Approval	1 day	Thu 6/17/21	Thu 6/17/21	
Construction Documents	50 days	Fri 6/18/21	Thu 8/26/21	
Award and Procure Manufactured Restroom Buildings	90 days	Fri 6/18/21	Thu 10/21/21	
DSA Review (Access Only)	30 days	Fri 8/27/21	Thu 10/7/21	
Bid & Award Site Package	25 days	Fri 10/8/21	Thu 11/11/21	
Construction	55 days	Fri 11/12/21	Thu 1/27/22	



Thoughts and Questions
